
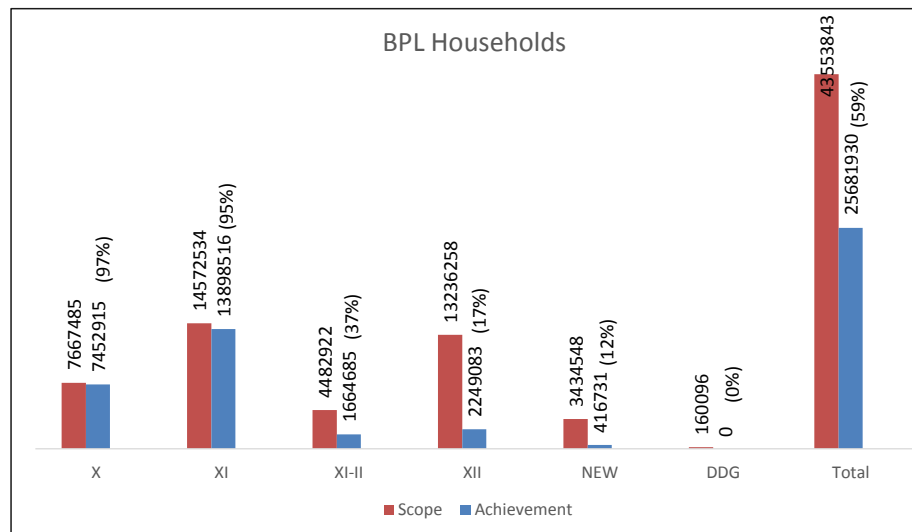
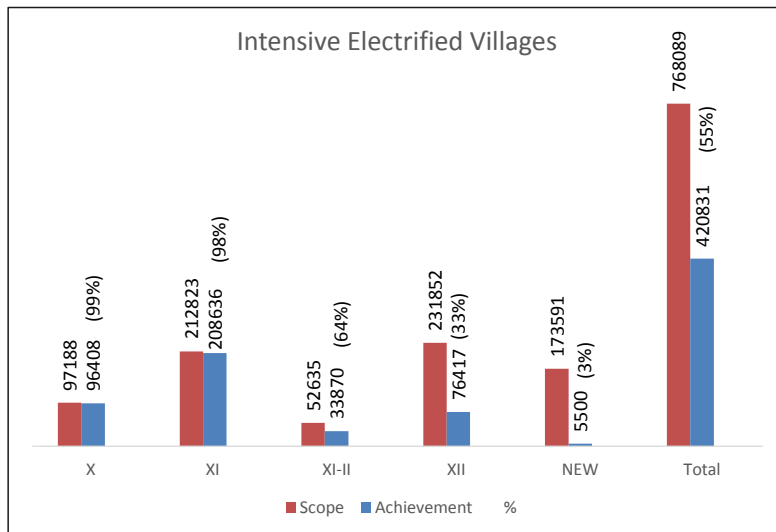
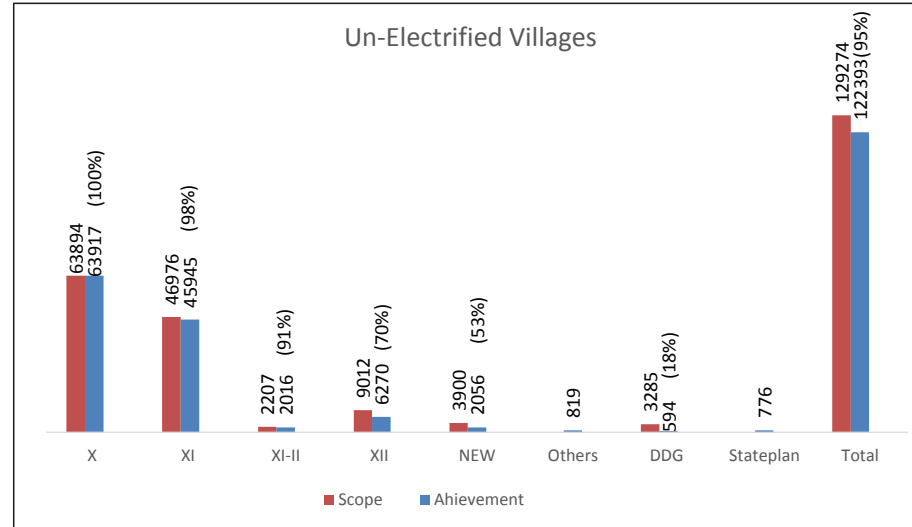


Scope & Cumulative Achievement as on 30-04-2017

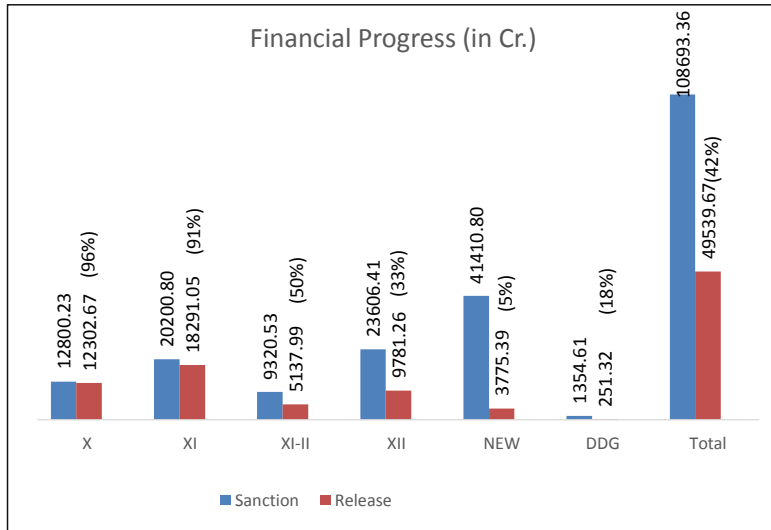

1. Scope & Cumulative Achievement

Plan	No. of Projects			Funds (Rs Crore)					Un-electrified villages (Nos.)			Intensive electrification of villages (Nos.)			BPL HH connections (Nos.)		
	Covered	Closed		Revised Sanction	Loan	Subsidy	Total Release	Scope	Cumulative achievement		Scope	Cumulative achievement		Scope	Cumulative achievement		
X	235	225	96%	12800.23	1221.04	11081.63	12302.67	96%	63894	63917	100%	97188	96408	99%	7667485	7452915	97%
XI	341	293	86%	20200.80	1707.12	16583.93	18291.05	91%	46976	45945	98%	212823	208636	98%	14572534	13898516	95%
XI-II	72	7	10%	9320.53	545.40	4592.58	5137.99	55%	2207	2016	91%	52635	33870	64%	4482922	1664685	37%
XII	273			23606.41	975.19	8806.06	9781.26	41%	9012	6270	70%	231852	76417	33%	13236258	2249083	17%
NEW	636			41410.80		3775.39	3775.39	9%	3900	2056	53%	173591	5500	3%	3434548	416731	12%
Others										819							
Total(DDUGJY RE)	1557	525	34%	107338.76	4448.76	44839.59	49288.35	46%	125989	121023	96%	768089	420831	55%	43393747	25681930	59%
DDG (XI)	157			100.39	2.73	44.43	47.16	47%	52	30	58%				8659		
DDG (XII)	354			112.17	1.47	37.42	38.90	35%	39	35	90%				14111		
DDG (NEW)	3709			1142.04	1.08	164.19	165.27	14%	3194	529	17%				137326		
DDG	4220			1354.61	5.28	246.04	251.32	19%	3285	594	18%				160096		
Stateplan										776							
Total	5777	525	9%	108693.36	4454.05	45085.63	49539.67	46%	129274	122393	95%	768089	420831	55%	43553843	25681930	59%

2. Performance report for FY 2017-18

Monthly Achievement During 2017-18

Month	Funds Drawn from MoP (Rs Cr)	UE Villages*	IE Villages	BPL HHs	DDG projects	Feeder Separation 11KV (Ckm)	Sub-Stations
Target	4814.00	4492	85000	4000000	3500	75000	400
April		234	6268	213730	18		3
Total achievement	0	234	6268	213730	18	0	3
Percentage achievement	0%	5%	7%	5%	1%	0%	1%

Planwise Achievement During April, 2017

Plan	UE Villages	IE Villages	BPL HHs	DDG projects	Feeder Separation 11KV (Ckm)	Sub-Stations
X, XI	16	30	352			1
XI - II		463	50635			
XII	81	5775	162605			2
NEW	49		138			
DDG	83			18		
Other						
Stateplan	5					
Reduction						
Total	234	6268	213730	18	0	3

* UEV progress has been taken from GARV APP

3.UE village progress as per GARV w.e.f 01-04-2015

Sl. No	States	Target UE Villages							Achieved UE Villages							Balance UE Villages						Uninhabited villages	To be electrified
		X-XI	XII	New	Offgrid	Stateplan	others*	Total	X-XI	XII	New	Offgrid	Stateplan	others *	Total	X-XI	XII	New	Offgrid	Stateplan	Total		
1	Arunachal Pradesh			433	970		175	1578			162	12		175	349			271	958		1229		1229
2	Assam	21	1011	600	582	128	550	2892	21	902	424	205	122	550	2224		109	176	377	6	668	110	558
3	Bihar	764	1940		43			2747	763	1559		1			2323	1	381		42		424		424
4	Chhattisgarh	396	5	198	471	10		1080	391	5	131	222	10		759	5		67	249		321		321
5	Himachal Pradesh			35				35			28				28			7			7	7	
6	Jammu & Kashmir	28	25	81				134	27	2	3				32	1	23	78			102		102
7	Jharkhand	1014	207	258	396	637	13	2525	945	170	135	9	620	13	1892	69	37	123	387	17	633	54	579
8	Karnataka			30	9			39			9	5			14			21	4		25		25
9	Madhya Pradesh	65	161	99	81		66	472	61	152	80	14		66	373	4	9	19	67		99	47	52
10	Manipur	72	204					276	63	136					199	9	68				77		77
11	Meghalaya	1		894	15		2	912	1		679			2	682			215	15		230		230
12	Mizoram	16		42				58	16		24				40			18			18		18
13	Nagaland		1	81				82		1	75				76			6			6	2	4
14	Odisha	1	2992	346	126		9	3474	1	2246	126	22		9	2404		746	220	104		1070	515	555
15	Rajasthan		236	95	97	63	4	495		210	95	93	24	4	426		26		4	39	69	68	1
16	Tripura		26					26		26					26								
17	Uttar Pradesh	569	868	80	11	1		1529	531	862	72	5			1470	38	6	8	6	1	59	53	6
18	Uttarakhand			56	20			76			17	6			23			39	14		53		53
19	West Bengal	8		14				22	8		9				17			5			5		5
Total		2955	7676	3342	2821	839	819	18452	2828	6271	2069	594	776	819	13357	127	1405	1273	2227	63	5095	856	4239

* Villages shifted from Offgrid to Grid

State Wise Scope & Cumulative Achievement of RE Projects

S. No.	Project name	Plan	Number of projects		Funds (Rs Crore)				Un-electrified villages (Nos.)				Intensive electrification of villages (Nos.)			BPL HH connections (Nos.)						
			covered	closed	Sanction	Loan	Subsidy	Total Release	Scope	GARV 18452 Bal UEV	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt				
1	Andhra Pr.	X	12	12	460.45	48.29	412.16	460.45	100%					14333		14333	100%	1771878		1771878	100%	
	Andhra Pr.	XI	4	4	95.77	10.67	86.00	96.66	101%					1781		1781	100%	226084		226084	100%	
	Andhra Pr.	NEW	16		921.74		140.45	140.45	15%					14822		5500	37%	713045		416593	58%	
	Andhra Pr.	DDG XI	57		16.61	1.43	12.85	14.27	86%									2225				
	Andhra Pr.	DDG XII	205		49.18	1.33	10.92	12.26	25%									6627				
	Andhra Pr.	DDG (NEW)	165		22.09													3048				
	Andhra Pr.	Total	459	16	1565.83	61.72	662.38	724.09	46%					30936		21614	70%	2722907		2414555	89%	
2	Arunachal Pr.	X	2	2	75.85	4.07	68.49	72.56	96%	236		236	100%	172		172	100%	9301		9301	100%	
	Arunachal Pr.	XI	14	14	953.98	25.47	845.69	871.17	91%	1842		1842	100%	1133		1133	100%	42320		42320	100%	
	Arunachal Pr.	NEW	16		267.20		47.98	47.98	18%	478	433	162	34%					6476				
	Arunachal Pr.	DDG (NEW)	1176		159.32					1176	970	12	1%					16582				
	Arunachal Pr.	Other									175											
	Arunachal Pr.	Reduction																				
	Arunachal Pr.	Total	1208	16	1456.35	29.54	962.16	991.70	68%	3732	1578	2427	65%	1305		1305	100%	74679		51621	69%	
3	Assam	X	3	3	199.54	20.39	179.62	200.01	100%	894		894	100%	1744		1744	100%	127573		127573	100%	
	Assam	XI	20	20	2430.28	242.64	2169.68	2412.32	99%	7458	20	7458	100%	11095		11095	100%	1082638		1082638	100%	
	Assam	Uninhabited									1											
	Assam	XII	16		1621.07	80.06	728.88	808.93	50%	1009	966	16	902	89%	10259			541953				
	Assam	Uninhabited									45											
	Assam	NEW	27		1274.10		80.65	80.65	6%	902	579	31	424	47%				20646				
	Assam	Uninhabited									21											
	Assam	DDG (NEW)	521		294.81	1.08	81.70	82.77	28%	521	545	17	205	39%				21781				
	Assam	Uninhabited									37											
	Assam	Other									550		550									
	Assam	Stateplan									128		122									
	Assam	Reduction																				
	Assam	Total	587	23	5819.80	344.16	3240.52	3584.68	62%	10784	2892	64	10555	98%	23098		12839	56%	1794591		1210211	67%
4	Bihar	X	26	25	2113.99	208.99	1887.31	2096.30	99%	16309		16602	100%	301		8	3%	787050		783692	100%	
	Bihar	XI	17	11	2208.05	182.24	1629.53	1811.77	82%	6948	5	6319	91%	5879	2	5796	99%	1558075		1460876	94%	
	Bihar	XI-II	11		2987.92	201.20	1560.68	1761.89	59%	1338	759	1128	84%	12790	420	9926	78%	2898328	49762	900443	31%	
	Bihar	XII	27		5220.65	218.34	1759.03	1977.37	38%	2927	1940	13	1559	53%	21833	913	9820	45%	5400947	112223	1018179	19%
	Bihar	NEW	38		5856.34		1000.92	1000.92	17%													
	Bihar	DDG (XI)									43		1									
	Bihar	Total	119	36	18386.95	810.78	7837.46	8648.24	47%	27522	2747	13	25609	93%	40803	1335	25550	63%	10644400	161985	4163190	39%
5	Chhattisgarh	X	3	3	220.19		178.11	178.11	81%	56		56	100%	3085		3085	100%	134459		134459	100%	
	Chhattisgarh	XI	13	9	948.88		754.42	754.42	80%	1554	386	1517	98%	11747		11404	97%	1059825	6	946923	89%	
	Chhattisgarh	XI-II	2		175.03		96.36	96.36	55%	126	10	115	91%	1077		925	86%	84334		49674	59%	

State Wise Scope & Cumulative Achievement of RE Projects

S. No.	Project name	Plan	Number of projects		Funds (Rs Crore)				Un-electrified villages (Nos.)			Intensive electrification of villages (Nos.)			BPL HH connections (Nos.)							
			covered	closed	Sanction	Loan	Subsidy	Total Release	Scope	GARV 18452 Bal UEV	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt				
	Jharkhand	DDG XII																				
	Jharkhand	DDG (NEW)	382		196.18				393	388	5	9	2%				21208					
	Jharkhand	Uninhabited								8												
	Jharkhand	Other								13		13										
	Jharkhand	Stateplan								636	5	620										
	Jharkhand	Uninhabited								1												
	Jharkhand	Total	445	12	8521.62	346.71	3092.73	3439.44	40%	20155	2525	38	19681	98%	35973	28	5662	16%	2445634	346	1276750	52%
12	Karnataka	X	17	17	563.48	54.72	493.90	548.62	97%	43			43	100%	16518		16518	100%	632667		632667	100%
	Karnataka	XI	8	8	301.21	28.45	242.76	271.21	90%	12			12	100%	5697		5697	100%	239943		239943	100%
	Karnataka	XI-II	2		81.04	7.87	70.07	77.93	96%						587		587	100%	27782		20080	72%
	Karnataka	XII	9		99.53	3.84	34.11	37.95	38%						9205		1977	21%	130785	441	89445	68%
	Karnataka	NEW	31		1754.52		104.07	104.07	6%	30	30		9	30%	21023				297788			
	Karnataka	DDG XII	37		27.50		5.30	5.30	19%	6	9		5	83%					2540			
	Karnataka	DDG (NEW)	2		0.61					3									123			
	Karnataka	Total	106	25	2827.89	94.87	950.21	1045.08	37%	94	39		69	73%	53030		24779	47%	1331628	441	982135	74%
13	Kerala	X	1	1	33.19	1.82	31.37	33.19	100%						37		37	100%	20715		20715	100%
	Kerala	XI	6	6	102.21	10.22	91.99	102.21	100%						557		557	100%	97646		97646	100%
	Kerala	XI-II	7	7	77.11	7.57	68.12	75.69	98%						493		493	100%	31944		31944	100%
	Kerala	NEW	14		485.37		86.93	86.93	18%						1315				98527			
	Kerala	DDG XII	15		5.32	0.14	1.24	1.38	26%										730			
	Kerala	Reduction																				
	Kerala	Total	43	14	703.20	19.75	279.65	299.40	43%						2402		1087	45%	249562		150305	60%
14	MP	X	8	8	502.44	48.30	433.23	481.54	96%	110			110	100%	9554		9554	100%	288184		288184	100%
	MP	XI	24	8	1378.51	120.30	1081.64	1201.95	87%	590	10		563	95%	22348		20641	92%	1023773		856180	84%
	MP	XI-II	20		983.20	59.03	521.25	580.28	59%	175	53		172	98%	15635		7544	48%	496714		261279	53%
	MP	Uninhabited								2												
	MP	XII	34		1430.93	78.84	704.98	783.82	55%	422	154		152	36%	25759		13947	54%	863166		338486	39%
	MP	Uninhabited								7												
	MP	NEW	50		2885.30		171.06	171.06	6%	136	90		80	59%	25662				525288			
	MP	Uninhabited								9												
	MP	DDG XI	25		27.17		10.57	10.57	39%	25			14	56%					2303			
	MP	DDG (NEW)	122		60.93					122									7100			
	MP	Uninhabited								29												
	MP	Other								66			66									
	MP	Reduction																				
	MP	Total	283	16	7268.48	306.49	2922.74	3229.22	44%	1580	472		1157	73%	98958		51686	52%	3206528		1744129	54%
15	Maharashtra	X	4	4	86.88	8.80	76.94	85.74	99%						4291		4291	100%	208969		208969	100%

State Wise Scope & Cumulative Achievement of RE Projects

S. No.	Project name	Plan	Number of projects		Funds (Rs Crore)				Un-electrified villages (Nos.)				Intensive electrification of villages (Nos.)			BPL HH connections (Nos.)						
			covered	closed	Sanction	Loan	Subsidy	Total Release	Scope	GARV 18452 Bal UEV	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt				
	Odisha	Reduction																				
	Odisha	Total	369	27	9088.11	471.48	4594.32	5065.80	56%	18400	3474	48	16784	91%	73936	1075	31022	42%	4596200	15830	2828451	62%
21	Punjab	X			3.00		3.00	3.00	100%													
	Punjab	XI	17	17	34.90	5.46	51.44	56.90	163%						6131		6131	100%	92988		92988	100%
	Punjab	NEW	20		251.98																	
	Punjab	Total	37	17	289.89	5.46	54.44	59.90	21%						6131		6131	100%	92988		92988	100%
22	Rajasthan	X	25	25	440.09	44.16	360.28	404.44	92%	1586			1586	100%	14664		14664	100%	470948		470948	100%
	Rajasthan	XI	15	14	762.48	73.07	643.00	716.07	94%	2571			2570	100%	18563		18563	100%	630404		629996	100%
	Rajasthan	XII	28		1453.19	63.25	569.09	632.34	44%		210		210		25397	3654	14168	56%	443757	31300	121073	27%
	Rajasthan	Uninhabited									26											
	Rajasthan	NEW	33		2819.37					104	95		95	91%	14517				234210			
	Rajasthan	DDG (NEW)									94		93									
	Rajasthan	Uninhabited									3											
	Rajasthan	Stateplan									24		24									
	Rajasthan	Uninhabited									39											
	Rajasthan	Other									4		4									
	Rajasthan	Reduction																				
	Rajasthan	Total	101	39	5475.13	180.48	1572.37	1752.86	32%	4261	495		4582	100%	73141	3654	47395	65%	1779319	31300	1222017	69%
23	Sikkim	X	2	2	90.72	8.30	74.53	82.83	91%	16			16	100%	158		158	100%	4189		4189	100%
	Sikkim	XI	2	2	121.73	10.85	97.35	108.20	89%	9			9	100%	254		254	100%	9412		9412	100%
	Sikkim	NEW	4		49.70										329				3413			
	Sikkim	Reduction																				
	Sikkim	Total	8	4	262.14	19.15	171.88	191.03	73%	25			25	100%	741		412	56%	17014		13601	80%
24	Tamilnadu	XI	26	26	341.20	35.30	312.63	347.93	102%						9673		9673	100%	501202		501202	100%
	Tamilnadu	XI-II	3		41.46	1.21	10.26	11.47	28%						729				24369		1192	5%
	Tamilnadu	NEW	27		924.09		165.51	165.51	18%						1016				897			
	Tamilnadu	Total	56	26	1306.75	36.51	488.40	524.91	40%						11418		9673	85%	526468		502394	95%
25	Telangana	X	5	5	202.83	20.63	186.23	206.86	102%						5681		5681	100%	504829		504829	100%
	Telangana	XI	5	5	107.90	20.74	85.01	105.75	98%						3495		3495	100%	204036		204036	100%
	Telangana	NEW	10		462.29		20.20	20.20	4%						9150				415166			
	Telangana	DDG XI	39		9.26		3.89	3.89	42%										1275			
	Telangana	Total	59	10	782.28	41.37	295.33	336.70	43%						18326		9176	50%	1125306		708865	63%
26	Tripura	X	1	1	34.94	3.31	31.63	34.94	100%	44			44	100%	72		72	100%	14260		14260	100%
	Tripura	XI	3	3	141.06	14.57	133.13	147.69	105%	97			97	100%	548		548	100%	102052		102052	100%
	Tripura	XII	8		316.23		168.82	168.82	53%	26	26		26	100%	778	4	302	39%	89604	2392	30048	34%
	Tripura	NEW	8		74.12										251				2816			
	Tripura	Total	20	4	566.36	17.88	333.57	351.45	62%	167	26		167	100%	1649	4	922	56%	208732	2392	146360	70%

State Wise Scope & Cumulative Achievment of RE Projects

S. No.	Project name	Plan	Number of projects		Funds (Rs Crore)				Un-electrified villages (Nos.)				Intensive electrification of villages (Nos.)			BPL HH connections (Nos.)						
			covered	closed	Sanction	Loan	Subsidy	Total Release	Scope	GARV 18452 Bal UEV	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt	Scope	Achmt 2017-18	Cum. Achmt				
	Total	NEW	636		41410.80		3775.39	3775.39	9%	3900	3273	49	2056	53%	173591		5500	3%	3434548	138	416731	12%
	Total	Uninhabited									69											
	Total	Other									819		819									
	Total	All Plans	1557	525	107338.76	4448.76	44839.59	49288.35	46%	125989	14792	146	121023	96%	768089	6268	420831	55%	43393747	213730	25681930	59%
	Total	DDG XI	157		100.39	2.73	44.43	47.16	47%	52		3	30	58%					8659			
	Total	DDG XII	354		112.17	1.47	37.42	38.90	35%	39			35	90%					14111			
	Total	DDG (NEW)	3709		1142.04	1.08	164.19	165.27	14%	3194		80	529	17%					137326			
	Total	DDG	4220		1354.61	5.28	246.04	251.32	19%	3285	2744	83	594	18%					160096			
	Total	Uninhabited									77											
	Total	Stateplan									798	5	776									
	Total	Uninhabited									41											
	Total	Reduction																				
	Grand Total	Total	5777	525	108693.36	4454.05	45085.63	49539.67	46%	129274	18452	234	122393	95%	768089	6268	420831	55%	43553843	213730	25681930	59%

Details of Sanction of New Projects under DDUGJY

S.No	State/UT	Category of State	Grid															Off-Grid					Total (Grid + Offgrid)			
			No. of Projects	Physical						Financial									No. of Projects	Physical		Financial		Financial		
				UE villages	IE Villages	SAGY villages	Habitations	RHHs (incl BPL)	BPL HHs	Component-wise cost (Rs Crore)										Fund Released (Rs. Cr)	Un-electrified villages (Nos.)	BPL HHs (in nos)	Sanctioned cost (Rs cr)	Fund Released (Rs. Cr)	Funds (Rs Cr)	
										Electrification of UE villages	SAGY	Metering	RHHs access	System Strengthening	Feeder Separation	PMA charges	Total Project Cost	Sanction							Release	
1	Andhra Pradesh	Others	16		14822	38	34855	904436	713045		10.08	7.25	409.70	490.12	0.00	4.59	921.74	140.45	165	0	3048	22.09		943.83	140.45	
2	Andaman & Nicobar		2			0	0				0.00	5.86	0.00	15.00	0.00	0.10	20.96				0			20.96	0.00	
3	Arunachal Pradesh	Special	16	478		3		14830	6476	199.22	8.44	58.21	0.00	0.00	0.00	1.33	267.20	47.98	1176	1176	16582	159.32		426.52	47.98	
4	Assam	Special	27	902	0	117	0	62538	20646	406.91	50.13	70.44	740.28	0.00	0.00	6.34	1274.10	80.65	521	521	21781	294.81	82.77	1568.91	163.42	
5	Bihar	Others	38	0		4	0	0	0	0.00	1.96	141.86	0.00	1243.70	4439.69	29.14	5856.35	1000.92		0	0	0.00		5856.35	1000.92	
6	Chhattisgarh	Others	27	177	2697	15	7129	137114	77795	58.93	4.46	41.66	432.05	308.03	411.99	6.29	1263.41	74.86	850	488	51322	269.21	82.49	1532.62	157.35	
7	Goa	Others	2			3						19.91				0.09	20.00			0	0	0.00		20.00	0.00	
8	Gujarat	Others	27	0	8941	19	12171	7425	5060	0.00	2.02	193.29	282.11	245.76	196.94	4.60	924.72	165.61		0	0	0.00		924.72	165.61	
9	Haryana	Others	21	0	2642	15	2873	237769	37890	0.00	10.78	12.64	64.58	189.13	37.37	1.57	316.07			0	0	0.00		316.07	0.00	
10	Himachal Pradesh	Special	12	35	3803	1	5145	14088	3288	6.04	0.03	13.51	59.42	78.16	1.15	0.79	159.10	13.46		0	0	0.00		159.10	13.46	
11	Jammu & Kashmir	Special	21	83	2250	6	4260	106632	46586	86.53	7.01	96.36	230.36	126.99	69.20	3.08	619.53			0	0	0.00		619.53	0.00	
12	Jharkhand	Others	24	368	11510	19		517417	340482	115.85	3.12	317.56	866.52	201.05	2199.49	18.52	3722.11		382	393	21208	196.18		3918.29	0.00	
13	Karnataka	Others	31	30	21023	150	33338	570861	297788	23.17	55.09	444.96	228.42	264.39	729.76	8.73	1754.52	104.07	2	3	123	0.61		1755.13	104.07	
14	Kerala	Others	14	0	1315	27	6550	191664	98527	0.00	59.14	159.16	181.59	83.07	0.00	2.41	485.37	86.93		0	0	0.00		485.37	86.93	
15	Madhya Pradesh	Others	50	136	25662	40	43277	1084714	525288	47.72	9.50	410.71	1053.31	530.16	819.54	14.35	2885.29	171.06	122	122	7100	60.93		2946.22	171.06	
16	Maharashtra	Others	37	0	30176	79	49387	1254077	395703	0.00	30.44	0.00	448.79	984.92	700.00	10.82	2174.97	252.87		0	0	0.00		2174.97	252.87	
17	Manipur	Special	3	0	182	3	309	19417	5794	0.00	0.68	0.00	54.01	0.00	0.00	0.27	54.96	4.68		0	0	0.00		54.96	4.68	
18	Meghalaya	Special	7	802	0	8	500	16614	8514	200.01	1.25	18.32	40.72	0.00	0.00	1.30	261.60	25.51	209	209	7151	40.55		302.15	25.51	
19	Mizoram	Special	8	29	15	1	45	2698	933	22.38	0.27	0.00	7.65	0.00	0.00	0.15	30.45			0	0	0.00		30.45	0.00	
20	Nagaland	Special	11	81	1102	2	1224	61298	21543	41.41	0.76	9.99	5.45	26.51	0.00	0.42	84.54	21.53		0	0	0.00		84.54	21.53	
21	Odisha	Others	30	521	5129	35	8594	184855	83035	301.91	36.81	440.93	424.44	302.21	140.00	8.23	1656.51	218.39	269	269	8821	95.05		1751.56	218.39	

Details of Sanction of New Projects under DDUGJY

S.No	State/UT	Category of State	Grid																Off-Grid				Total (Grid + Offgrid)				
			No. of Projects	Physical						Financial										No. of Projects	Physical		Financial		Financial		
				UE villages	IE Villages	SAGY villages	Habitations	RHHs (incl BPL)	BPL HHs	Component-wise cost (Rs Crore)											Fund Released (Rs. Cr)	Un-electrified villages (Nos.)	BPL HHs (in nos)	Sanctioned cost (Rs cr)	Fund Released (Rs. Cr)	Funds (Rs Cr)	
										Electrification of UE villages	SAGY	Metering	RHHs access	System Strengthening	Feeder Separation	PMA charges	Total Project Cost	Sanction	Release								
22	Punjab	Others	20	0	0	20	25	0	0	0.00	5.02	84.82	0.00	160.01	0.88	1.25	251.98			0	0	0.00		251.98	0.00		
23	Puducherry		2	0	17	0	0	7891	0	0.00	0.00	15.05	2.32	2.68	0.00	0.10	20.15	1.20			0			20.15	1.20		
24	Rajasthan	Others	33	104	14517	34	40853	722360	234210	23.42	11.43	370.44	1132.03	602.97	665.05	14.03	2819.37			0	0	0.00		2819.37	0.00		
25	Sikkim	Special	4		329	2	980	12266	3413		6.94	7.35	35.16			0.25	49.70			0	0	0.00		49.70	0.00		
26	Tamilnadu	Others	27	0	1016	0	1468	7068	897	0.00	0.00	119.65	56.74	617.16	125.94	4.60	924.09	165.51			0	0	0.00		924.09	165.51	
27	Telangana	Others	10	0	9150	15	23782	567463	415166	0.00	15.36	5.16	308.27	131.20	0.00	2.30	462.29	20.20			0	0	0.00		462.29	20.20	
28	Tripura	Special	8	0	251	0	388	12536	2816	0.00	0.00	36.59	28.63	8.53	0.00	0.37	74.12			0	0	0.00		74.12	0.00		
29	Uttar Pradesh	Others	75	84	16639	92	25133	684332	58132	9.48	59.75	294.05	1143.15	2147.76	3257.69	34.56	6946.44	722.06			0	0	0.00		6946.44	722.06	
30	Uttarakhand	Special	13	56	0	5	0	0	0	60.68	3.75	43.77	111.29			618.32	4.19	842.00	71.21	13	13	190	3.31		845.30	71.21	
31	West Bengal	Others	19	14	395	0	585	58987	31305	46.86	0.60	441.22	1729.94	862.35	1159.98	21.20	4262.15	386.24			0	0	0.00		4262.15	386.24	
32	Dadra & Nagar Haveli	Others	1		8	1		249	216		0.21	1.68	0.93	2.15		0.02	5.00			0	0	0.00		5.00	0.00		
	Total		636	3900	173591	754	302871	7461599	3434548	1650.52	395.03	3882.40	10077.86	9624.01	15572.99	206.00	41410.80	3775.39	3709	3194	137326	1142.05	165.27	42552.84	3940.65		

New Projects: NIT and Award Status

SI No.	State Name	Total No. of Projects	Awarded/ LOI issued	Departmental	Bids opened & Under Evaluation	NIT Issued & Bids yet to be opened	NIT yet to be issued	Remarks for non award for balance works (other than VE works)
1	Andhra Pradesh	16	15		1			NIT yet to be issued for Chipurapalli Society
2	Andaman & Nicobar	2					2	Requested MoP for Special Status
3	Arunachal Pradesh	16	14		2			Tirap under court case and Changlang due to non-receipt of BG.
4	Assam	27			27			
5	Bihar	38	38					
6	Chhattisgarh	27	27					
7	Goa	2					2	Due to limited fund, only Metering component will be executed. DPRs submitted, in-principle approval conveyed
8	Gujarat	27		27				
9	Haryana	21	6		5	10		a) UHBVNL, BoD for all 10 project is 26.04.17 & 04.05.17
10	Himachal Pradesh	12		1	1	10		10 projects - NIT issued & less bids received, HPSEB to take decision
11	Jammu & Kashmir	21			14	7		a). Kashmir & Ladhakh province, 11 projects, 6 under evaluation & 5 NIT yet to be issued by PGCIL
12	Jharkhand	24	4		20	0		Out of balance 20 project, 12 evaluated & in advance stage of award
13	Karnataka	31	16		9	0	6	1. 9 projects , evaluated and in advance stage of award
14	Kerala	14		14				
15	Madhya Pradesh	50	39		7	4	0	
16	Maharashtra	37	18		19			Part-A (S/S work) & part B (Lines & LT works)
17	Manipur	3	1	2				
18	Meghalaya	7	7					NIT for addl 7 projects shall be issued after receipt of approval
19	Mizoram	8	8					Awarded (Included in villages works)
20	Nagaland	11		11			0	
21	Odisha	30	30					
22	Punjab	20			20			PSERC direction awaited
23	Puducherry	2					2	NIT yet to be issued
24	Rajasthan	33	30		3	0		
25	Sikkim	4					4	DPR uploaded, NIT under process and likely to be floated by 30.04.17
26	Tamilnadu	27		27				
27	Telangana	10	5		4		1	NIT yet to be issued for Sircilla society
28	Tripura	8			8	0		All are under evaluation Except DTR & Metering
29	Uttar Pradesh	75	60		15			
30	Uttarakhand	13				13		UPCL to request for Modification in DPR portal. Technical bid opened, Price bid to be open on 26.04.17
31	West Bengal	19	0		19			2 Pkgs- (a). Pkg-1 (Feeder segregation & RHH) (b) Pkg - 2 (33 KV works)
32	Dadra & Nagar Haveli	1					1	NIT yet to be issued
	Total	636	318	82	174	44	18	

6. Status of Sanctioned DDG projects

S.No	State	Implementing Agency	Sanction in plan	Technology Adopted	No. of projects	No. of Districts	Capacity (KW)	UEVs covered	Villages/Hamlets covered	No. of Households covered (Incl. BPL)	BPL HHs Achievement	No. of BPL Households covered	Effective project cost (Rs. in lakhs)	No. of Projects commissioned	No. of UEVs Commissioned	Fund Released (Rs. In Lakh)
1	Andhra Pradesh	APEPDCL	XI	SPV	57	1	365	0	57	2225	1884	2225	1660.58	57	0	1427.4581
		APSPDCL	XII	SPV	11	1	143.5	0	11	1035	398	1035	469.44	5	0	0
		APEPDCL	XII	SPV	194	2	894	0	194	5592	3315	5592	4448.69	166	0	1225.95
		APEPDCL	DDUGJY	SPV	165	1	518	0	165	3048	0	3048	2209.39	0	0	0
Sub Total Andhra Pradesh					427		1920.5	0	427	11900	5597	11900	8788.1	228	0	2653.4081
2	Assam	APDCL	DDUGJY	SPV + SHLS	521	14	8949	521	521	45520	825	21781	29480.84	85	85	8277.27
Sub Total Assam					521		8949	521	521	45520		21781	29480.84	85	85	8277.27
3	Arunachal Pradesh	APEDA	DDUGJY	STANDALONE	1176	17		1176	1176	16582	0	16582	15931.65	0	0	0
Sub Total Arunachal Pradesh					1176		0	1176	1176	16582	0	16582	15931.65	0	0	0
4	Bihar	BSHPC	XI	41 projects are Hybrid of Biomass	0	0	0	0	0	0	0	0	0	0	0	0
Sub Total Bihar					0		0	0	0	0		0	0	0	0	0
4	Chhattisgarh	CREDA	XI	SPV	9	2	102	8	9	645	490	645	345	9	8	304.29
		CREDA	XII	SPV	87	3	523	24	87	3923	4490	3923	2431	87	24	1995.74
		CREDA	DDUGJY	SPV+SHLS	850	16	4723	488	870	51322		51322	26920.96	534	204	8249.36
Sub Total Chhattisgarh					946		5348	520	966	55890	4980	55890	29696.96	630	236	10549.39
5	Jharkhand	DVC	XII	SPV	0	0	0	0	0	0	0	0	0	0	0	0
		JREDA	DDUGJY	SPV + SHLS	382	8	6689	393	393	25726	0	21208	19617.9	0	0	0
Sub Total Jharkhand					382		6689	393	393	25726	0	21208	19617.9	0	0	0
6	Karnataka	GESCOM (1) & CSEC (1)	XII	SPV	2	2	63	0	1	124	0	124	175.86	0	0	0
		CESC	XII	SPV	25	3	390	6	31	1716		1598	1962	6	2	529.74
		MESCOM	XII	SPV	0	0	0	0	0	0	0	0	0	0	0	0
		CESCL	XII	SPV	10	2	138.2	0	11	828		818	612	0	0	0
		MESCOM	DDUGJY	SHLS	2	3		3	3	123		123	61	0	0	0
Sub Total Karnataka					39		591.2	9	46	2791	0	2663	2810.86	6	2	529.74
7	Kerala	KSEB	XII	SPV	15	1	131.5	0	15	731	239	730	531.83	7	0	138.21
Sub Total Kerala					15		131.5	0	15	731	239	730	531.83	7	0	138.21
8	Madhya Pradesh	MPUVNL	XI	SPV	25	4	528	25	91	2859	2410	2303	2717.02	23	23	1057.29
		DDUGJY	SPV + SHLS	122	13	2780	122	202	12975		7100	6092.55	0	0	0	
Sub Total Madhya Pradesh					147		3308	147	293	15834	2410	9403	8809.57	23	23	1057.29
9	Meghalaya	MeECL	XII	SPV	3	1	154	3	3	751		248	389.4	0	0	0
		MePDCL	DDUGJY	STANDALONE	209	7		209	209	7151		7151	4055	0	0	0
Sub Total Meghalaya					212		154	212	212	7902	0	7399	4444.4	0	0	0
10	Odisha	OREDA	XII	SPV	7	1	65.5	6	7	268		43	197	0	0	0
		DDUGJY	SPV + SHLS	269	11	3480	269	272	11889		8821	9504.69	0	0	0	
Sub Total Odisha					276		3545.5	275	279	12157	0	8864	9701.69	0	0	0
12	Rajasthan	AVVNL	XII	SPV	0	0	0	0	0	0	0	0	0	0	0	0
		AVVNL	XII	SPV	0	0	0	0	0	0	0	0	0	0	0	0
		JVVNL	XII	SPV	0	0	0	0	0	0	0	0	0	0	0	0
Sub Total Rajasthan					0		0	0	0	0	0	0	0	0	0	
11	Telangana	TSNPDCL	XI	SPV	39	2	202	0	39	1275	849	1275	925.88	34	0	389.15
Sub Total Telangana					39	2	202	0	39	1275	849	1275	925.88	34	0	389.15
12	Uttar Pradesh	UPNEDA	XI	SPV	7	2	79	6	7	500		351	346	7	6	1262.47
		UPNEDA	XI	SPV	5	2	308	5	15	2055		1031	2140.8	0	0	
		UPNEDA	XI	SPV	13	1	190	6	13	1210		536	1397.3	13	6	
Sub Total Uttar Pradesh					25		577	17	35	3765	0	1918	3884.1	20	12	1262.47
13	Uttarakhand	UREDA	XI	Small Hydro	2	2	300	2	10	460		293	506.26	1	1	275.49
		UPCL	DDUGJY	SPV + SHLS	13	1	102	13	13	633		190	330.5	0	0	0
Sub Total Uttarakhand					15		402	15	23	1093	0	483	836.76	1	1	275.49
Total XI Plan					157		2074	52	241	11229	5633	8659	10038.84	144	44	4716.1481
Total XII Plan					354		2502.7	39	360	14968	8442	14111	11217.22	271	26	3889.64
Total DDUGJY					3709		27241	3194	3824	174969	825	137326	114204.48	619	289	16526.63
Total XI, XII and DDUGJY					4220		31817.7	3285	4425	201166	14900	160096	135460.5	1034	359	25132.4181

Details of closed projects and Infrastructure created there under

S.No.	States	No. of Projects Closed				Final coverage & Executed Infrastructure as per closure																	
		X	XI	XI-II	Total	UEV/DEV (nos.)	IEV (nos.)	BPL Hhs (nos.)	Final Completion Cost (Rs. Lakhs)	New 33/11 kV S/s (nos.)	Aug of S/s (nos.)	33 kV line	DTs (nos.)								11 kV line (kms.)	LT line (kms.)	
													5 KVA	10 KVA	15 KVA	16 KVA	25 KVA	40 KVA	63 KVA	Total			Cap. (MVA)
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22		
1	Andhra Pradesh	12	4	0	16	0	16114	1897972	54709.29293	8	16	250.37	0	40	15236	2910	339		0	18525	283.975	4375.727	15801.539
2	Arunachal Pradesh	2	14	0	16	2078	1305	39121	102758.52	22	1	709.5	1491	689	0	494	517		0	3191	35.174	9154.15	2426.18
3	Assam	3	20	0	23	7991	12114	1108385	244215.13	31	1	539.248	0	1085	0	19468	8371		0	25867	476.896	30153.115	34639.53
4	Bihar	25	11	0	36	16303	1025	859259	210908.53	81	22	1623.235	0	3070	0	23154	6915	22	0	33161	574.919	24118.389	26610.819
5	Chhattisgarh	3	9	0	12	121	10106	303327	43933.71	11	37	1.25	0	4052	857	2548	2206		0	9663	149.293	4567.1149	7105.0905
6	Gujarat	3	22	0	25	0	16144	745460	31469.23	0	0	0.00	3	346	0	1574	731		48	2702	49.96	1113.03	8861.45
7	Haryana	4	14	0	18	0	5137	193762	15524.19	0	0	0.00	0	0	0	260	4867		459	5586	154.75	1675.64	695.83
8	Himachal Pradesh	1	11	0	12	90	7896	15293	29748.51	1	8	0	0	15	0	237	1796		187	2235	60.623	1469.461	5843.112
9	Jammu & Kashmir	3	9	0	12	125	1161	31208	19249.25	4	8	26.414	0	2	0	187	1654		0	1843	44.362	1338.96	2984.65
10	Jharkhand	7	5	0	12	9072	3241	556249	118225.45	43	28	1004.589	0	13324	0	7562	2282		0	23168	311.282	16538.919	17121.906
11	Karnataka	17	8	0	25	55	21150	821863	79247.17011	0	5	0	0	0	86	0	13888		0	13974	348.49	3783.245	15444.3
12	Kerala	1	6	7	14	0	1087	113305	19750.41	2	5	2.50	0	0	0	0	1825		0	1825	45.63	1939.04	3563.69
13	Madhya Pradesh	8	8	0	16	165	12175	420002	71910.37	4	32	23.89	0	2523	721	4919	7145		0	15308	293.374	11918.97	10537.50
14	Maharashtra	4	30	0	34	0	35325	1198861	66320.46	3	14	0.00		191	1123	279	7108		14	8715	201.80	3526.50	9845.60
15	Meghalaya	2	3	0	5	1022	2425	84383	26795.13	1	0	5.77	34	412	0	686	1166		0	2298	44.416	2533.15	5906.94
16	Mizoram	2	6	0	8	170	517	26210	31213.71	4	0	200	0	0	0	0	742			742	18.55	1407.75	811.21
17	Nagaland	2	9	0	11	102	855	41788	21047.61	10	26.5	216.5	0	0	0	46	849		0	748	22.185	1140.04	1079.85
18	Odisha	4	23	0	27	3946	7524	685481	81301.28	8	51	106.6	0	10466	0	8066	2065		0	20597	285.341	11796.044	18605.65
19	Punjab	0	17	0	17	0	6131	72988	3490.44	0	0	0	0	0	0	0	4198		0	4198	104.95	555.3	38.39
20	Rajasthan	25	14	0	39	2909	24600	760824	82522.07	2	0	49.49	0	0	0	22473	5735		0	28208	502.943	13876.03	31567.56
21	Sikkim	2	2	0	4	25	412	13601	21244.72	0	0	0	0	282	0	0	122		0	404	5.87	608.06	791.88
22	Tamil Nadu	0	26	0	26	0	9673	501202	34120.25	0	0	0	0	0	0	4724	5405		0	10129	210.709	2646.53	1959.21
23	Telangana	5	5	0	10	0	9176	708865	31073.06	2	0	8.17	0	653	9448	4	536		1	10642	161.777	3150.909	11897.42
24	Tripura	1	3	0	4	141	620	106329	17421.06	6	1	102.5	0	962	0	626	237		0	1825	25.561	871.92	1879.69
25	Uttar Pradesh	63	0	0	63	27140	2991	888013	368493.19	197	281	2937.198	0	76379	0	27388	9076		0	112843	1428.9	48300.835	22069.552
26	Uttarakhand	13	0	0	13	1514	10042	202954	78200.09	6	13	118.448	0	508	0	9118	2872		0	12498	222.768	8582.528	11496.44
27	West Bengal	13	14	0	27	4183	10682	1223899	139377.58	13	1	178.237	0	7514	0	4558	6174		0	18246	302.418	10362.685	24447.348
Grand Total		225	293	7	525	77152	229628	13620604	2044270.41	459	551	8103.91	1528	122513	27471	141281	98821	22	709	389141	6366.91	221504.03	294032.34

State-wise Implementing agency- wise Sub-station Status (X,XI,XI,phase- II, XII & New plan)

Sl. No	Name of State	Implementing Agency	RE Components of DDUGJY															New S/S Sanctioned under New Plan	Commissioned 2017-18
			Nos.of S/s Sanctioned					Nos.of Commissioned & Charged					Bal.nos. of S/s yet to be erected						
			X	XI	XI-II	XII	Total	X	XI	XI-II	XII	Total	X	XI	XI-II	XII	Total		
1			4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	Andaman&Nicobar	ED&AN Admin																5	
2	Andhra Pradesh	EPDCL	4	3			7	4	3			7							
		SPDCL	1				1	1				1							
	Total Andhra Pradesh		5	3			8	5	3			8							
3	Arunachal Pradesh	Power Deptt.	2	20			22	2	20			22							
4	Assam	APDCL	3	23		20	46	3	23			26				20	20		
		PGCIL	3	4			7	3	4			7							
	Total Assam		6	27		20	53	6	27			33				20	20		
5	Bihar	NBPDCL		35	19	38	92		30	11	1	42		5	8	37	50	171	
		SBPDCL		2	17	8	27		2	14	1	17			3	7	10	117	
		NHPC	11	29			40	11	29			40							
		PGCIL	71	10			81	71	10			81							
	Total Bihar		82	76	36	46	240	82	71	25	2	180		5	11	44	60	288	
6	Chhattisgarh	NESCL		1			1		1			1							
		PGCIL		2			2		2			2							
		CSPDCL		7	1		8		7	1		8						80	
	Total Chhattisgarh			10	1		11		10	1		11						80	
7	Gujarat	UGVCL																4	
		MGVCL																16	
		DGVCL																5	
	Total Gujarat																	25	
8	Haryana	DHBVNL																5	
		UHBVNL																9	
	Total Haryana																	14	
9	Himachal Pradesh		1				1	1				1						16	
10	Jammu & Kashmir	NHPC	3	11			14	3	11			14							
		JKSPDCL	1	5			6	1	5			6						40	
	Total J & K		4	16			20	4	16			20						40	
11	Karnataka	HESCOM																4	
12	Kerala	KSEB		2			2		2			2						2	
13	Jharkhand	DVC	24	18			42	24	18			42							
		JBVNL	33			11	44	28				28	5			11	16	104	
		NTPC	4	28			32	4	27			31		1			1		1
	Total Jharkhand		61	46		11	118	56	45			101	5	1		11	17	104	
14	Maharashtra	MSDCL		3			3		3			3						215	
15	Madhya Pradesh	NESCL	4				4	4				4							
		MPPOKVCL		1			1		1			1						52	
		MPMKVCL				34	34				20	20				14	14	18	
		MPPsKVCL																65	
	Total MP		4	1		34	39	4	1		20	25				14	14	135	
16	Manipur	Power Deptt.	2	9		1	12	2	7			9		2		1	3		
17	Meghalaya	MSEB		5			5		2			2		3			3		
18	Mizoram	Power Deptt.	1	3		6	10	1	3			4				6	6		
19	Nagaland	Power Deptt.	2	8		1	11	2	8			10				1	1		

State-wise Implementing agency- wise Augmentation Sub-station Status (X,XI,XI,phase- II, XII & New plan)

Sl. No	Name of State	Implementing Agency	RE Components of DDUGJY																	Commissioned 2017-18
			Nos.of Augu S/s Sanctioned					Nos.of Commissioned & Charged					Bal.nos. Augu of S/s yet to be erected							
			X	XI	XI-II	XII	New	Total	X	XI	XI-II	XII	New	Total	X	XI	XI-II	XII	New	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	
		WESCO					36	36										36	36	
		SOUTHCO					17	17										17	17	
		Total Odisha					66	66										66	66	
21	Rajasthan	AVVNL																		
		JVVNL																		
		JdVVNL					5	5										5	5	
		Total Rajasthan					5	5										5	5	
22	Tamil Nadu	TANGEDCO					184	184										184	184	
23	Telangana	TNPDCL																		
		TSSPDCL																		
		Total Telangana																		
24	Tripura	TSECL																		
		PGCIL																		
		NEEPCO																		
		Total Tripura																		
25	Uttar Pradesh	DVVNL					342	342										342	342	
		MVVNL					64	64										64	64	
		PGCIL			30	6	36	36			30	6	36							
		PSVVNL					82	82										82	82	
		PUVVNL					265	265										265	265	
		Total Uttar Pradesh			30	6	753	789			30	6	36					753	753	
26	Uttarakhand	UPCL																		
27	West Bengal	NESCL																		
		PGCIL																		
		WBSEDCL				11	103	114				11	11					103	103	
		NHPC																		
		Total West Bengal				11	103	114				11	11					103	103	
	Grand Total		72	138	30	243	2314	2652	60	117	30	177	384		1		66	2169	2236	

Status of Power Supply to Rural Areas

MONTH : March- 2017

SL. No.	Name of the State	Average Hours of Power Supply in a day To Rural Areas
1	2	3
1	Andhra Pradesh	24.00
2	Arunachal Pradesh	12.30
3	Assam	19.00
4	Bihar	17.02
5	Chhattisgarh	23.00
6	Gujarat	24.00
7	Haryana	12.53
8	Himachal Pradesh	24.00
9	Jammu & Kashmir	13.75
10	Jharkhand	17.77
11	Karnataka	16.40
12	Kerala	23.00
13	Madhya Pradesh	23.60
14	Maharashtra	23.32
15	Manipur	21.50
16	Meghalaya	21.50
17	Mizoram	12.00
18	Nagaland	18.00
19	Odisha	22.20
20	Punjab	24.00
21	Rajasthan	22.00
22	Sikkim	17.50
23	Tamil Nadu	24.00
24	Telangana	24.00
25	Tripura	23.50
26	Uttar Pradesh	18.28
27	Uttarakhand *	23.52
28	West Bengal	24.00

*Uttarakhand January month data has been included.
