


Review, Planning & Monitoring (RPM) Meeting

Village Electrification on Mission Mode under DDUGJY




सपना नहीं सच्चाई है, बिजली हमारे घर आई है,
अच्छे दिनों की शुरुआत है, अंधेरे में भी जगमग रात है।

12th April 2016, New Delhi

Team INDIA, made it Happen!!



**UNPRECEDENTED
GROWTH RATE OF
ELECTRIFICATION**

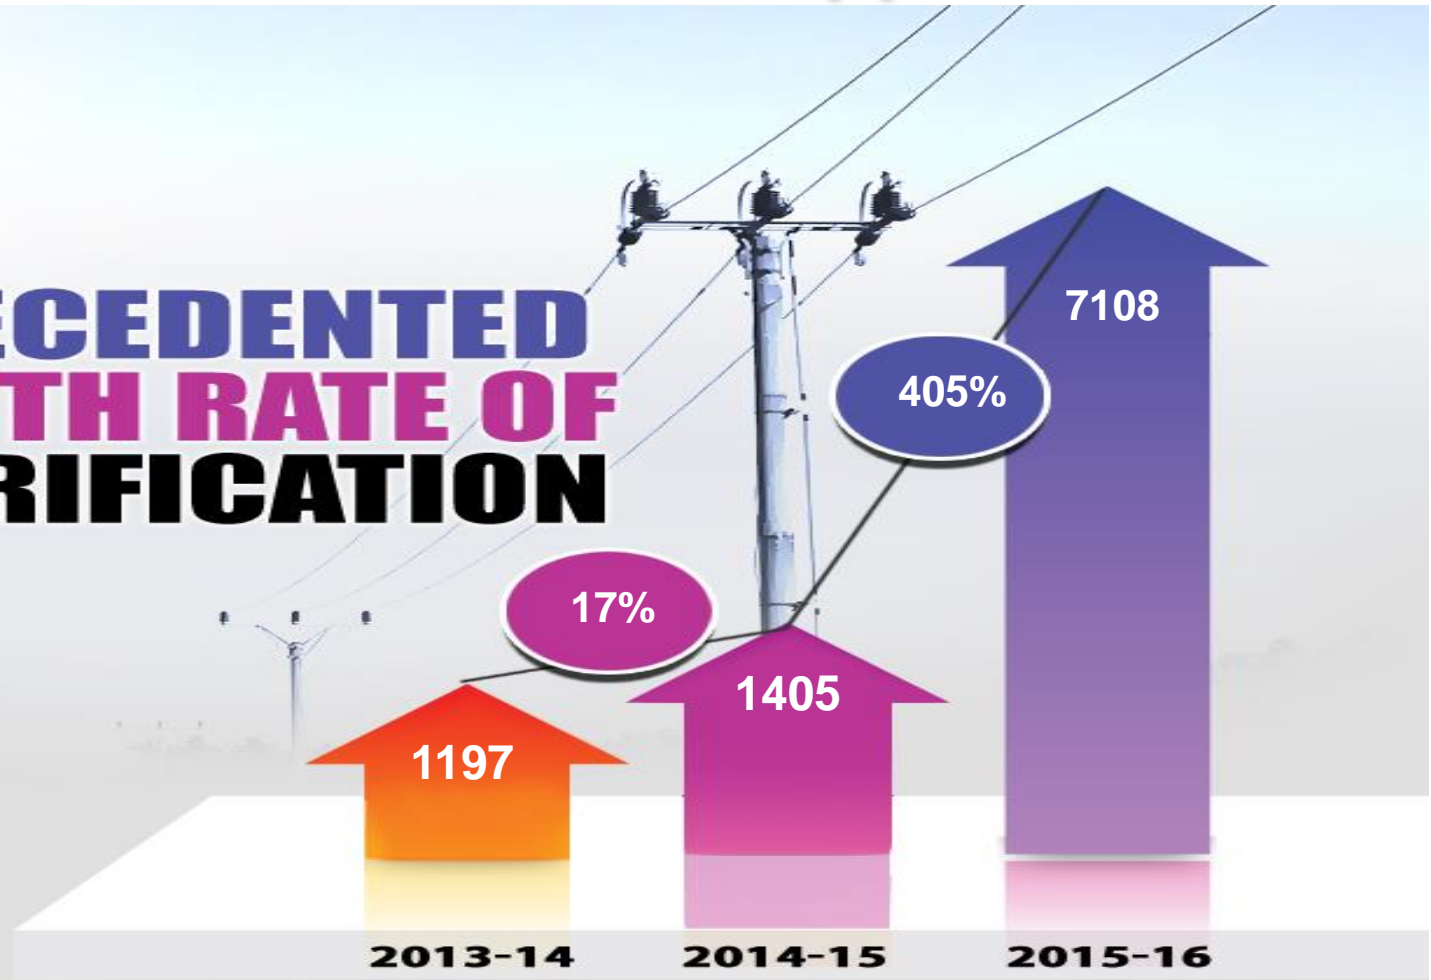

गाँव का विकास गर्व के साथ

Village Electrification - National View

Total inhabited un-electrified villages : **18452**
(as on 31.03.2015)

Villages electrified during 2015-16 : **7108**
(up to 31.03.2016)

Uninhabited villages : **441**

Balance un-electrified villages : **11344**
(as on 31.03.2016)

- **To be electrified through Grid** - **8243**
(All sanctioned, Awarded- 6184)
- **To be electrified through Off-Grid** - **2621**
(All Sanctioned, Awarded- 158)
- **To be electrified under State Plan** - **480**

***All the remaining 11344 un-electrified villages
are targeted for electrification by December 2016***

Electrification of Un-electrified villages in FY 2016-17: Target

State	Grid (un-awarded)	Off-Grid(un-awarded)	Total (un-awarded)
All India	8243 (2059)	3101 (2943)	11344 (5002)
1 Arunachal Pr.	- 351 (351)	1053 (1053)	1404 (1404)
2 Assam	948 (301)	1002 (1002)	1950 (1303)
3 Jharkhand	- 1366 (237)	409 (409)	1775 (646)
4 Odisha	2210 (625)		2210 (625)
5 Chhattisgarh	176	499 (372)	675 (372)
6 Meghalaya	- 894 (340)	17 (17)	911 (357)
7 J & K	107 (107)		107 (107)
8 Madhya Pr.	- 166	92 (69)	258 (69)
9 Uttar Pradesh	- 224 (68)		224 (68)

Electrification of Un-electrified villages in FY 2016-17: Target

State	Grid (un-awarded)	Off-Grid(un-awarded)	Total (un-awarded)
10 Karnataka	30 (30)	9 (3)	39 (33)
11 Uttarakhand	56	20 (18)	76 (18)
12 Bihar	-	993	993
13 Rajasthan	-	332	332
14 Manipur	201		201
15 Nagaland	-	82	82
16 Mizoram	42		42
17 Himachal Pr.	-	34	34
18 Tripura	17		17
19 West Bengal	-	14	14
G-Total	8243(2059)	3101(2943)	11344 (5002)

Electrification of Un-electrified villages in FY 2016-17: Schedule

In 2016 →	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
All India	415	688	873	1376	1459	1531	1716	1692	1594
1 Arunachal Pr.							475	472	457
2 Assam	62	80	95	112	148	150	445	440	418
3 Bihar	62	74	110	258	248	241			
4 Chhattisgarh	12	15	54	76	75	71	120	122	130
5 Himachal Pr.				7	9	18			
6 J & K							38	36	33
7 Jharkhand	52	168	215	244	232	218	224	218	204
8 Karnataka				2	2	2	13	12	8
9 Madhya Pr.	31	33	32	34	29	30	25	23	21

Electrification of Un-electrified villages in FY 2016-17: Schedule

In 2016 →	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
10 Manipur	5	12	15	60	56	53			
11 Meghalaya		2	18	105	175	254	124	122	111
12 Mizoram				11	12	19			
13 Nagaland				13	31	38			
14 Odisha	154	252	270	320	298	291	223	220	182
15 Rajasthan	15	28	36	84	86	83			
16 Tripura				4	7	6			
17 Uttar Pradesh	22	24	25	27	27	31	24	22	22
18 Uttarakhand			3	13	19	23	5	5	8
19 West Bengal				6	5	3			
G-Total	415	688	873	1376	1459	1531	1716	1692	1594

Mission Mode... Facilitating Measures

- Any village yet to be sanctioned???
- Award all remaining un-awarded projects/villages ASAP.
- SBD squeezed to 6 months for village electrification
- Better use of the GARV App, for identifying the gaps in milestones
- Quality module in GARV App under testing stage.
- All Households in the 18452 villages to be given access to electricity
- A New App under preparation for DDUGJY pan India.
- On pilot basis, GVA appointed in each District of UP

thank you..

Actions by States/Discoms

- **Commissioning of sub-stations:**
Bihar-41, Jharkhand-16, Manipur-11, West Bengal-4, Chhattisgarh-1
- **Award of XII Plan 28 projects:**
J&K - 3, Jharkhand-8, Odisha-6, Uttar Pradesh-9, Rajasthan-2
- **Award of XI Plan Phase-II 10 projects:**
Uttar Pradesh-4, Haryana-3, MP-3
- **Slow progress:**
Jharkhand (Latehar, Palamu & Garhwa), Chhattisgarh(Bastar)

Details of balance un-electrified villages (as on 31.03.2016)

Sl. No.	State	Total UE Villages as on 31.03.2015	Electrified villages as on 31.03.2016	Villages To be Electrified as on 31.03.2016
1	Arunachal Pradesh	1578	174	1404
2	Assam	2892	942	1950
3	Bihar	2747	1754	993
4	Chhattisgarh	1080	405	675
5	Himachal Pradesh	35	1	34
6	Jammu & Kashmir	134	27	107
7	Jharkhand	2525	750	1775
8	Karnataka	39	0	39
9	Madhya Pradesh	472	214	258
10	Manipur	276	75	201
11	Meghalaya	912	1	911
12	Mizoram	58	16	42
13	Nagaland	82	0	82
14	Odisha	3474	1264	2210
15	Rajasthan	495	163	332
16	Tripura	26	9	17
17	Uttar Pradesh	1529	1305	224
18	Uttarakhand	76	0	76
19	West Bengal	22	8	14
G-Total		18452	7108	11344



Un-inhabited Villages

S. No.	State	Uninhabited Villages
1	Himachal Pradesh	7
2	Madhya Pradesh	3
3	Odisha	420
4	Rajasthan	11
Total		441



XII Plan Un-awarded Projects

S. No.	Name of Project	Date of Sanction by REC	PIA	Project Cost (Rs. Lakhs)	Scope (Nos.)			Remarks
					UE Villages	IE Villages	Rural HHs (Incl. BPL)	
Jammu & Kashmir								
1	Doda	1/Mar/14	JKPDC	4037.4		187	14558	Bid prices 40% higher, under negotiation, State to take decision to bear balance amount.
2	Ramban	1/Mar/14	JKPDC	2020.7	1	89	8582	
3	Kishtwar	1/Mar/14	JKPDC	4070.1	24	76	19771	
3	Total J&K			10128.2	25	352	42911	
Jharkhand								
1	Ranchi	1/Mar/14	JBVNL	14804.6	171	1098	181921	Board approval received. NIT under process.
2	Khunti	1/Mar/14	JBVNL	4906.0	66	624	51647	
3	East Singhbhum	1/Mar/14	JBVNL	8027.9		1542	50928	
4	Deogarh	1/Mar/14	JBVNL	9200.4		1793	38481	
5	Sahibganj	1/Mar/14	JBVNL	7284.2		1602	86719	
6	Jamtara	1/Mar/14	JBVNL	6440.8		998	23293	
7	Pakur	1/Mar/14	JBVNL	6798.0		1158	52213	
8	Saraikela-Kharsawan	1/Mar/14	JBVNL	2702.5		1088	67738	single bid received, Bid opening date extended to 16.04.2016.
8	Total Jharkhand			60164.4	237	9903	552940	
Odisha								
1	Sambalpur	31/Dec/13	NESCL	10820.0	2	1303	129716	Earlier Contract to M/s Variegate terminated. Re-tendered, Technical bids opened and under evaluation.
2	Jharsuguda	31/Dec/13	NESCL	6683.0		351	53626	
3	Deogarh	31/Dec/13	NESCL	3396.0	16	462	41195	
4	Angul	31/Dec/13	NESCL	6141.0	33	1341	88337	
5	Keonjhar	31/Dec/13	NESCL	17800.0	48	1848	182610	
6	Bolangir	31/Dec/13	NESCL	11060.0	5	1744	309688	
6	Total Odisha			55900.0	104	7049	805172	

XII Plan Un-awarded Projects

S. No.	Name of Project	PIA	Date of Sanction by REC	Project Cost (Rs. Lakhs)	Scope (Nos.)			Remarks
					UE Villages	IE Villages	Rural HHs (Incl. BPL)	
Uttar Pradesh								
1	Baghpat	PsVVNL	31/Dec/13	5772.6		267	58072	LOI issued. Contract Agreement yet to be executed.
2	Sambhal (total 8 blocks)	PsVVNL	10/Sep/13	14856.2	7	865	170638	LOI issued. Contract Agreement yet to be executed.
3	Meerut (total 12 blocks)	PsVVNL	6/Jan/14	4932.6		487	24245	LOI issued. Contract Agreement yet to be executed.
4	Rampur (06 Block(s))	PsVVNL	6/Jan/14	15929.2	8	1070	149992	LOI issued. Contract Agreement yet to be executed.
5	Amethi	MVVNL	31/Dec/13	10311.7		983	119830	LOI issued. Contract Agreement yet to be executed.
6	Ambedkar Nagar	MVVNL	31/Dec/13	6963.6		1687	126619	LOI issued. Contract Agreement yet to be executed.
7	Hardoi	MVVNL	31/Dec/13	11060.5		2048	184035	LOI issued. Contract Agreement yet to be executed.

XII Plan Un-awarded Projects

S. No.	Name of Project	PIA	Date of Sanction by REC	Project Cost (Rs. Lakhs)	Scope (Nos.)			Remarks
					UE Villages	IE Villages	Rural HHs (Incl. BPL)	
Uttar Pradesh								
8	Lucknow	MVVNL	31/Dec/13	12028.4		481	119374	Date of bid opening extended to 12.04.2016.
9	Sitapur (5 Tehsils)	MVVNL	31/Dec/13					Date of bid opening extended to 12.04.2016.
9	Total Uttar Pradesh			115702.4	15	11350.0	1430544.0	
Rajasthan								
1	Dungarpur	AVVNL	27/Sep/13	13892.5		816	90065	Re-tendered. Bids under evaluation
2	Bikaner	JdVVNL	27/Sep/13	15600.9		772	70463	
2	Total Rajasthan			29493.4		1588	160528	
28	GRAND TOTAL			296345.4	381	33727.0	3254464.0	

XI Plan Ph-II Un-awarded Projects

- **Uttar Pradesh-** 2 Projects yet to be awarded
 - i. Hardoi- Sanctioned on Mar'12. Project Retendered. Bids to be opened on 23.04.2016.
 - ii. Behraich- Sanctioned on Mar'12. Project Retendered. Bids to be opened on 23.04.2016.
- **Haryana-** 3 Projects (Gurgaon, Faridabad & Palwal) yet to be awarded. All projects sanctioned on Dec'11. Projects retendered and bids under evaluation..

Sub-Stations yet to be commissioned

- **Bihar – 41 Sub-stations**

(Begusarai-2, Khagaria-2, Samastipur-1, Araria- 3, Siwan- 10, Kishanganj- 2, Purnea- 4, Banka- 2, Bhojpur- 3, Gaya- 2, Nalanda- 6, Patna- 2, Nawada-1 & Rohtas-1)

- **Jharkhand – 16 Sub-stations**

(Garhwa-3, Latehar-2, Saraikela-2, West Singhbhum- 1, Chatra- 6, Ranchi- 2)

- **Manipur – 11 Sub-stations**

(Chandel-2, Senapati-1, Ukhrul-2, Bishnupur- 1, Churachandpur- 2, Thoubal- 1, Imphal West - 1, Imphal East - 1)

- **West Bengal – 4 Sub-stations** (Cooch Behar – 1, Purulia – 3)

- **Chhattisgarh – 2 Sub-stations** (Bastar – 1, Jashpur – 1)
